


SUMC Renovation Update and Look Ahead

So far our project is progressing well. We have not uncovered any major problems. We are on schedule and within budget.

Phase 1 (Men's Restroom) wraps up in the next couple of weeks and we will move on to Phase 2 (Women's Restroom and Kitchen). Here is where we need your help and patience.

On Monday, March 27, we will begin Phase 2 and that means we will not have any access to our existing public restrooms and kitchen. Phase 2 will take approximately 8 weeks to complete. During this time, the new Men's Restroom will serve as a temporary Women's Restroom and the two existing Restrooms on the 2nd floor will serve as temporary Men's Restrooms. Since the temporary Men's Restrooms are not ADA (American with Disabilities Act) accessible, we must provide an ADA compliant facility for the Men. This will be an ADA temporary toilet on the sidewalk by the west side glass doors.

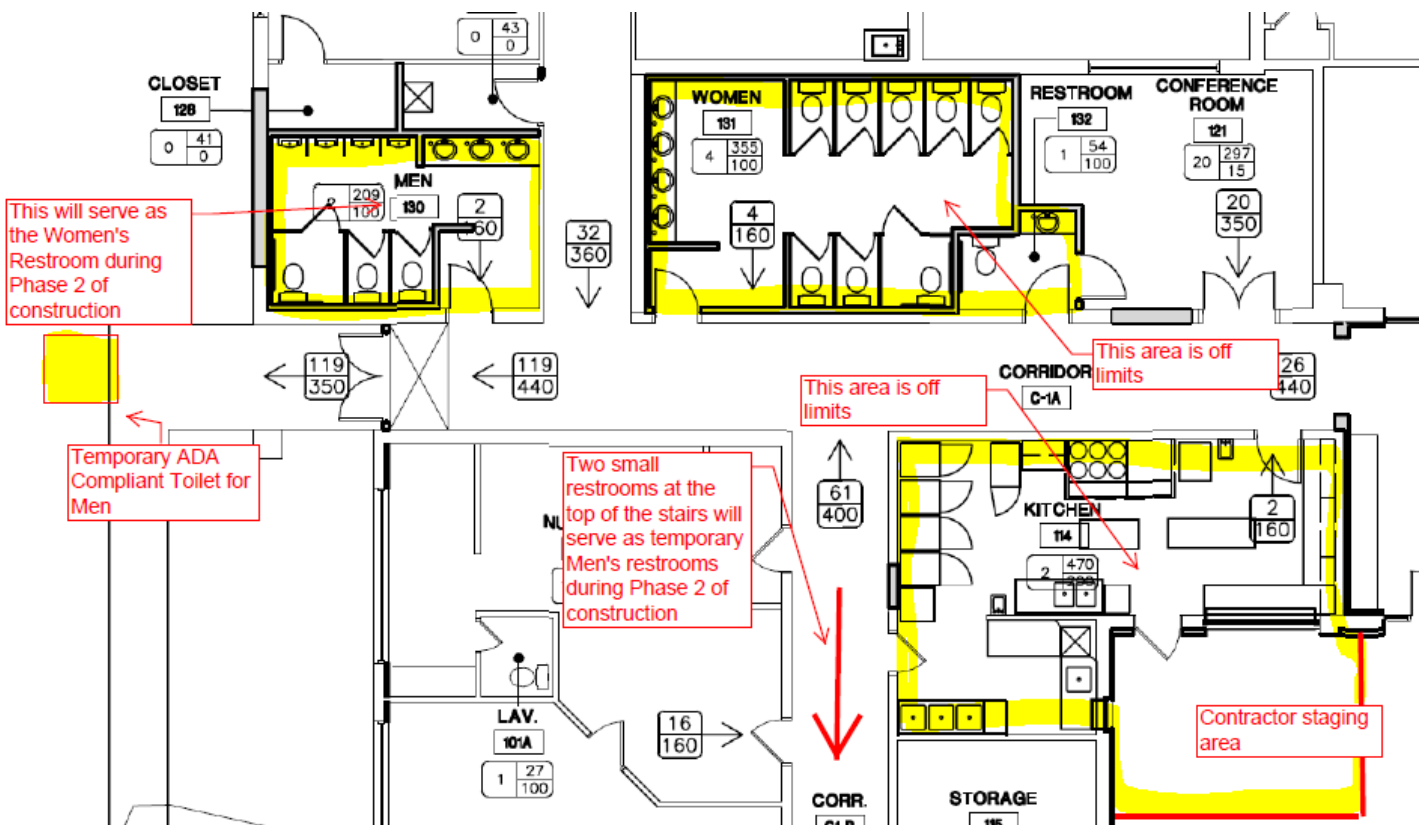

We will have signage in place. Please familiarize yourself with our plan and if you see a confused visitor, please help them. We appreciate your patience and help as we make our way through Phase 2.
